
**SUPPLY SCOPE (distributor quantities issue, no prices): we supply the pre-cut Nudura ICF forms only; the stock forms, accessories and alignment system are supplied by the distributor. All other structure and information shown is supplied in good faith for coordination only and must be checked by the relevant professional.**

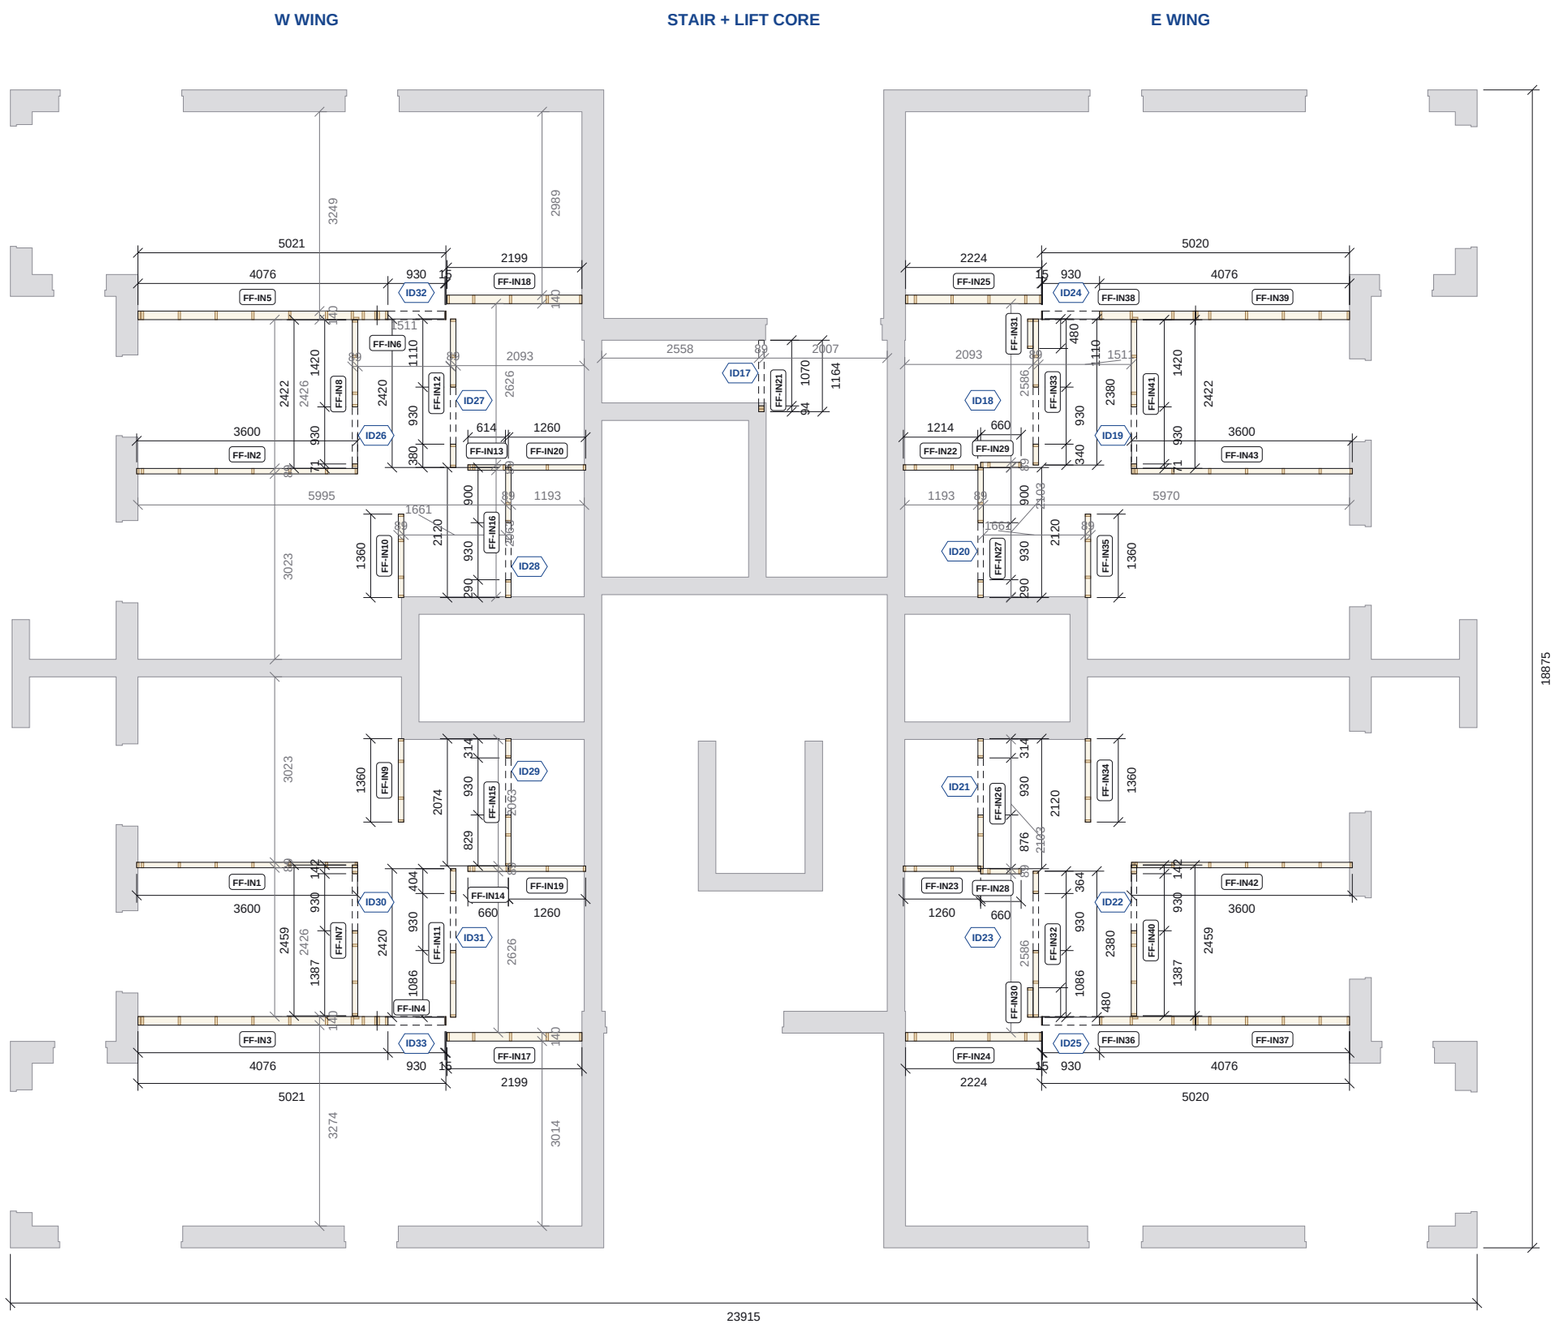


## FIRST FLOOR TIMBER PARTITIONS PLAN

Scale 1:100 @ A3 | Plan cut at 1200 above floor level

Partition panel, studs cut at plan level | Panel joint | Nudura ICF shell (context only) | Door opening, head over

0 1 2 3 4 5m

**QUOTATION - NOT FOR CONSTRUCTION**

Do not scale. All dimensions in mm. Check all dimensions on site.

## FIRST FLOOR SCHEDULES

### PARTITION SUMMARY

| Zone | Studs | Use | Panels | Run m |
|---|---|---|---|---|
| Core | 38x89 C16 @600 | partition | 1 | 1.2 |
| E wing | 38x140 C16 @600 | flat wall + 9 OSB | 6 | 14.5 |
| E wing | 38x89 C16 @600 | partition | 16 | 28.6 |
| W wing | 38x140 C16 @600 | flat wall + 9 OSB | 6 | 14.4 |
| W wing | 38x89 C16 @600 | partition | 14 | 27.6 |
| **Total** | | | **43** | **86.3** |

Too many panels on this floor for a per-panel schedule: panels grouped by zone, studs and use (marks on the plan). Wet-room walls at 400 centres; 38x140 walls carry 9 OSB one side.

### DOOR OPENING SCHEDULE

| Label | Width | Height | Head |
|---|---|---|---|
| ID17 | 1070 | 2100 | 2100 |
| ID18 | 930 | 2100 | 2100 |
| ID19 | 930 | 2100 | 2100 |
| ID20 | 930 | 2100 | 2100 |
| ID21 | 930 | 2100 | 2100 |
| ID22 | 930 | 2100 | 2100 |
| ID23 | 930 | 2100 | 2100 |
| ID24 | 930 | 2100 | 2100 |
| ID25 | 930 | 2100 | 2100 |

| Label | Width | Height | Head |
|---|---|---|---|
| ID26 | 930 | 2100 | 2100 |
| ID27 | 930 | 2100 | 2100 |
| ID28 | 930 | 2100 | 2100 |
| ID29 | 930 | 2100 | 2100 |
| ID30 | 930 | 2100 | 2100 |
| ID31 | 930 | 2100 | 2100 |
| ID32 | 930 | 2100 | 2100 |
| ID33 | 930 | 2100 | 2100 |

Structural opening sizes. Head level above underside of the bottom rail.

### PARTITION TIMBER (THIS FLOOR, ALL FLATS)

| Section | Pieces | Run m | 4.8m lengths |
|---|---|---|---|
| 38x89 C16 | 386 | 581.7 | 128 |
| 38x140 C16 | 166 | 267.5 | 59 |
| 15x140 C16 | 4 | 10.7 | 3 |

Studs, rails and noggins from the model. Order lengths = run / 4.8m +5%, not cut-optimised.

### NOTES

1. Internal partitions only, non-load-bearing (TLSTF): drawn partitions 38x89 C16 studs at 600 centres with 38x89 head and bottom rails, 15 board each side (119); wet-room walls at 400 centres for pattressing; the walls drawn on the wall layer inside the flats (Tom 19.10: timber, not ICF) 38x140 C16 at 600 + 9 OSB one side. Panel marks refer to the partition schedule.
2. External, compartment and core walls are Nudura ICF (grey), shown for context only: read with the ICF drawings. Partitions are set out from the ICF internal face and adjacent partitions (grey set-out strings).
3. Floors are concrete: sole plates fixed to the slab (DPC under) at <= 600 c/c; heads restrained to the SF metal-deck slab soffit with slotted deflection head clips (by others to confirm).
4. Door openings are structural opening sizes. Head level above underside of the bottom rail. All flats of the floor shown (block plan as drawn, front at the bottom). Dimensions to timber frame faces. Check all dimensions on site.

### REVISIONS

| REV | DATE | DESCRIPTION |
|---|---|---|
| Q01 | 19.10.26 | First issue |

Nudura™ BuildEase

| CLIENT | PROJECT |
|---|---|
| Ian Piercy (Distributor) for Ramsey Town Commissioners | Close Woirrey / Albert Road, Ramsey, Isle of Man |

DRAWING TITLE

**BLOCK 1 (12 FLATS) - FIRST FLOOR TIMBER PARTITIONS**

Internal stud partitions, panels and door openings

| SCALE | SIZE | DATE |
|---|---|---|
| 1:100 | A3 | 19.10.26 |
| DRAWN | CHECKED | APPROVED |
| TS | | |

| STATUS | DRAWING No. | REV |
|---|---|---|
| QUOTATION | ES26-071-TF-02 | Q01 |
