
SUPPLY SCOPE (distributor quantities issue, no prices): we supply the pre-cut Nudura ICF forms only; the stock forms, accessories and alignment system are supplied by the distributor. All other structure and information shown is supplied in good faith for coordination only and must be checked by the relevant professional.

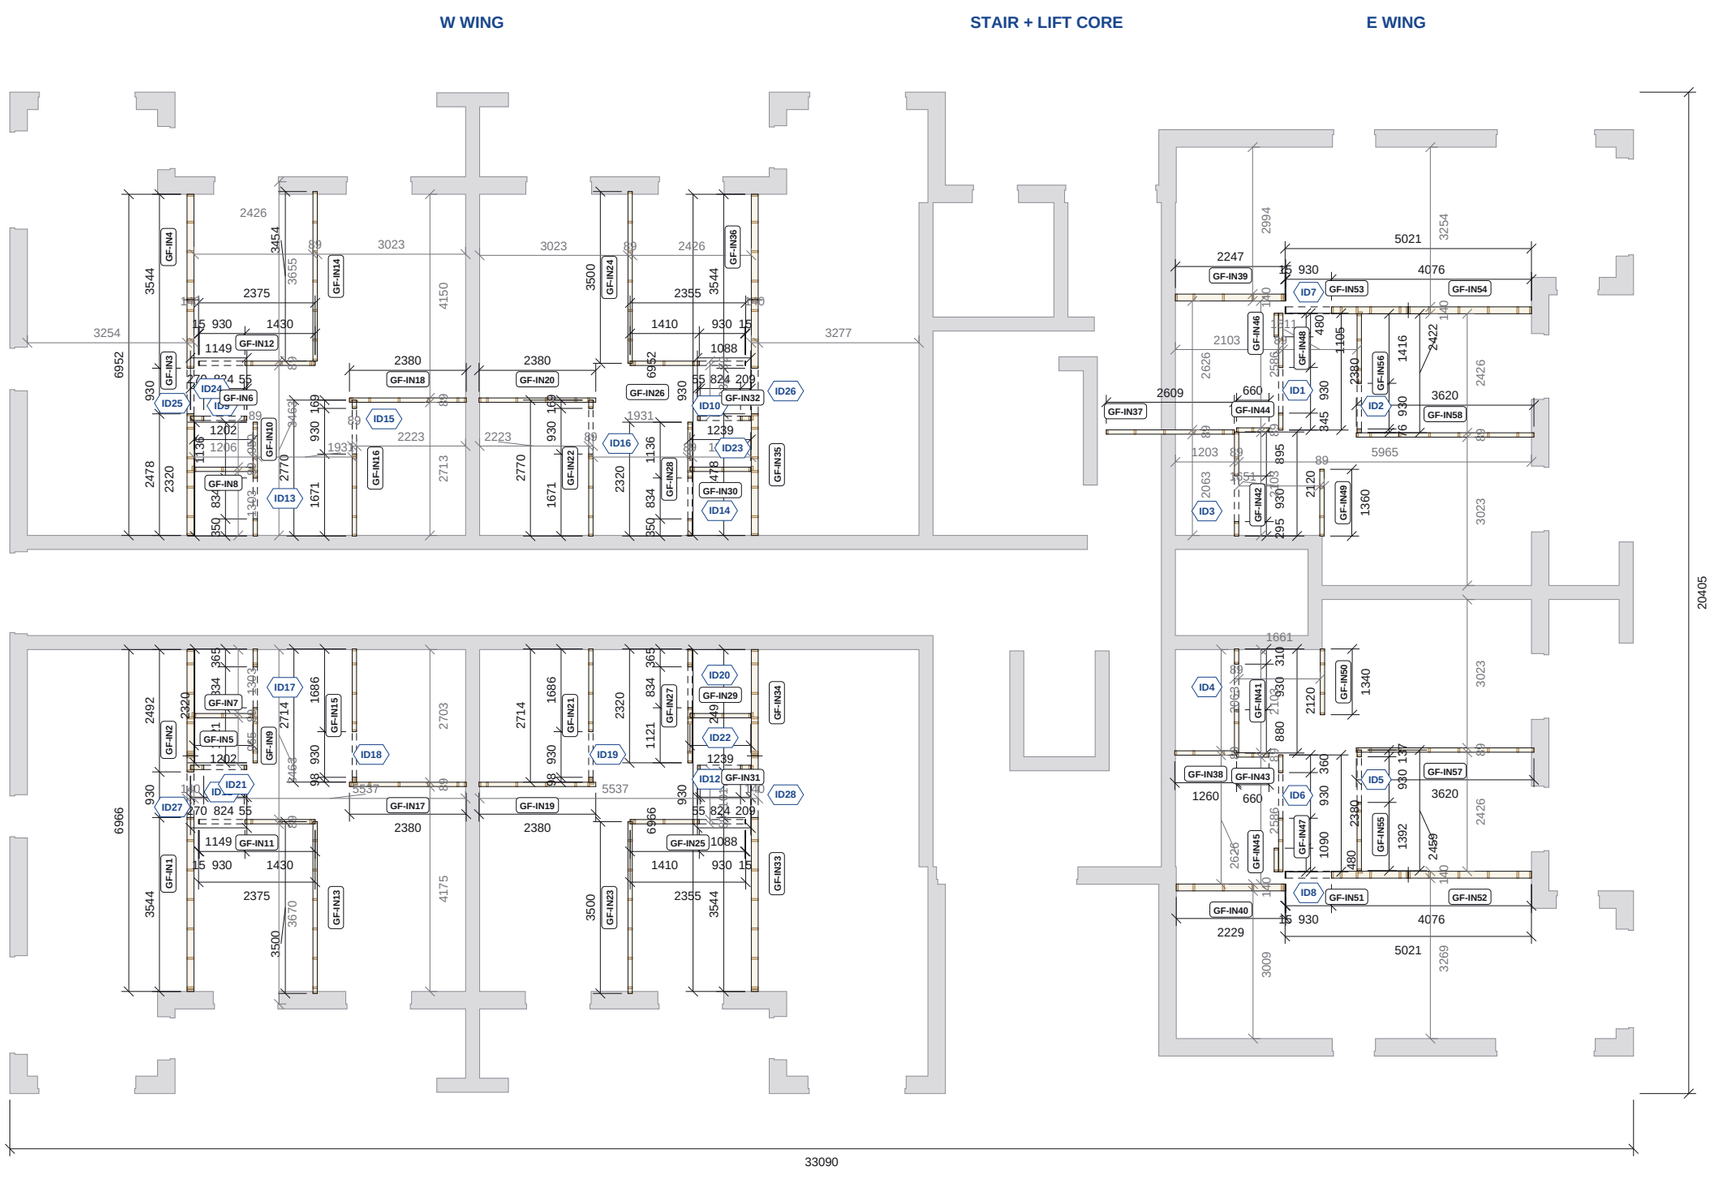

GROUND FLOOR TIMBER PARTITIONS PLAN

Scale 1:125 @ A3 | Plan cut at 1200 above floor level

Partition panel, studs cut at plan level | Panel joint | Nudura ICF shell (context only) | Door opening, head over

0 1 2 3 4 5m

QUOTATION - NOT FOR CONSTRUCTION

Do not scale. All dimensions in mm. Check all dimensions on site.

GROUND FLOOR SCHEDULES

PARTITION SUMMARY

Zone	Studs	Use	Panels	Run m
E wing	38x140 C16 @600	flat wall + 9 OSB	6	14.5
E wing	38x89 C16 @600	partition	16	30.0
W wing	38x140 C16 @600	flat wall + 9 OSB	8	27.8
W wing	38x89 C16 @600	partition	28	62.5
Total			**58**	**134.8**

Too many panels on this floor for a per-panel schedule: panels grouped by zone, studs and use (marks on the plan). Wet-room walls at 400 centres; 38x140 walls carry 9 OSB one side.

DOOR OPENING SCHEDULE

Label	Width	Height	Head	Label	Width	Height	Head
ID1	930	2100	2100	ID15	930	2100	2100
ID2	930	2100	2100	ID16	930	2100	2100
ID3	930	2100	2100	ID17	834	2100	2100
ID4	930	2100	2100	ID18	930	2100	2100
ID5	930	2100	2100	ID19	930	2100	2100
ID6	930	2100	2100	ID20	834	2100	2100
ID7	930	2100	2100	ID21	824	2100	2100
ID8	930	2100	2100	ID22	824	2100	2100
ID9	930	2100	2100	ID23	824	2100	2100
ID10	930	2100	2100	ID24	824	2100	2100
ID11	930	2100	2100	ID25	930	2100	2100
ID12	930	2100	2100	ID26	930	2100	2100
ID13	834	2100	2100	ID27	930	2100	2100
ID14	834	2100	2100	ID28	930	2100	2100

Structural opening sizes. Head level above underside of the bottom rail.

PARTITION TIMBER (THIS FLOOR, ALL FLATS)

Section	Pieces	Run m	4.8m lengths
38x89 C16	637	987.1	216
38x140 C16	250	408.7	90
15x89 C16	4	10.8	3
15x140 C16	2	5.4	2

Studs, rails and noggins from the model. Order lengths = run / 4.8m +5%, not cut-optimised.

NOTES

1. Internal partitions only, non-load-bearing (TLSTF): drawn partitions 38x89 C16 studs at 600 centres with 38x89 head and bottom rails, 15 board each side (119); wet-room walls at 400 centres for pattressing; the walls drawn on the wall layer inside the flats (Tom 19.10: timber, not ICF) 38x140 C16 at 600 + 9 OSB one side. Panel marks refer to the partition schedule.
2. External, compartment and core walls are Nudura ICF (grey), shown for context only: read with the ICF drawings. Partitions are set out from the ICF internal face and adjacent partitions (grey set-out strings).
3. Floors are concrete: sole plates fixed to the slab (DPC under) at <= 600 c/c; heads restrained to the FF metal-deck slab soffit with slotted deflection head clips (by others to confirm).
4. Door openings are structural opening sizes. Head level above underside of the bottom rail. All flats of the floor shown (block plan as drawn, front at the bottom). Dimensions to timber frame faces. Check all dimensions on site.

REVISIONS

REV	DATE	DESCRIPTION
Q01	19.10.26	First issue

Nudura™ BuildEase

CLIENT	PROJECT
Ian Piercy (Distributor) for Ramsey Town Commissioners	Close Woirrey / Albert Road, Ramsey, Isle of Man

DRAWING TITLE

BLOCK 2 (18 FLATS) - GROUND FLOOR TIMBER PARTITIONS

Internal stud partitions, panels and door openings

SCALE	SIZE	DATE
1:125	A3	19.10.26
DRAWN	**CHECKED**	**APPROVED**
TS		

STATUS	DRAWING No.	REV
QUOTATION	ES26-071-TF-04	Q01
